ID	Task Name	Duration	Start	Finish
1	**Eatern Regional Reclaimed Water Distribution System - Phase II Transmission Main Contract 1B / P# 2983**	1 day?	Fri 7/17/09	Fri 7/17/09
2				
3	Contract Execution	0 days	Fri 7/17/09	Fri 7/17/09
4				
5	Preconstruction Conference	0 days	Wed 7/22/09	Wed 7/22/09
6				
7	Mobilization	0 days	Mon 7/27/09	Mon 7/27/09
8	Establish Erosion Control	0 days	Mon 7/27/09	Mon 7/27/09
9	Clearing (Plant-Golfway)	5 days	Mon 7/27/09	Fri 7/31/09
10	Dewatering	5 days	Mon 8/3/09	Fri 8/7/09
11	Begin 42" Install Sta. 1+00 - Golfway	13 days	Mon 8/10/09	Wed 8/26/09
12	Establish MOT along Golfway	5 days	Mon 8/3/09	Fri 8/7/09
13	Switch Traffic	0 days	Sun 8/9/09	Sun 8/9/09
14	Jack n Bore Alafaya (@ Golfway)	12.5 days	Mon 8/10/09	Wed 8/26/09
15	Pressure Testing/Pig	10 days	Wed 8/26/09	Wed 9/9/09
16	Begin 42" Install Sta. 20+00 - 50+30	25 days	Thu 8/27/09	Wed 9/30/09
17	Pressure Testing/Pig	10 days	Thu 10/1/09	Wed 10/14/09
18	Roadway Restoration (Golfway)	20 days	Thu 10/15/09	Wed 11/11/09
19	Establish MOT along Woodbury	3 days	Thu 10/1/09	Mon 10/5/09
20	Jack n Bore Sta. 90+00	10 days	Wed 8/26/09	Wed 9/9/09
21	Jack n Bore Sta. 108+69	10 days	Wed 9/9/09	Wed 9/23/09
22	Jack n Bore Sta. 117+7	10 days	Wed 9/23/09	Wed 10/7/09
23	Begin 42" Install 50+30 -160+00	119 days	Tue 10/6/09	Fri 3/19/10
24	Pressure Testing/Pig (Under Roadway)	10 days	Fri 10/30/09	Thu 11/12/09
25	Pressure Testing/Pig	15 days	Mon 3/22/10	Fri 4/9/10
26	Woodburt Roadway Restoration	30 days	Fri 11/13/09	Thu 12/24/09
27	Begin Restoration (Grassing)	82 days	Fri 12/25/09	Mon 4/19/10
28	Jack n Bore Sta. 82+37	10 days	Wed 10/7/09	Wed 10/21/09
29	Jack n Bore Sta. 89+36	10 days	Wed 10/21/09	Wed 11/4/09
30	Jack n Bore Sta. 94+28 Underhill	25 days	Wed 11/4/09	Wed 12/9/09
31	Jack n Bore Sta. 125+92 E-Way 408	25 days	Wed 12/9/09	Wed 1/13/10
32	Jack n Bore Sta. 134+64	10 days	Wed 1/13/10	Wed 1/27/10
33	Jack n Bore Sta. 150+83	10 days	Wed 1/27/10	Wed 2/10/10
34	Jack n Bore Sta. 159+11	10 days	Wed 2/10/10	Wed 2/24/10

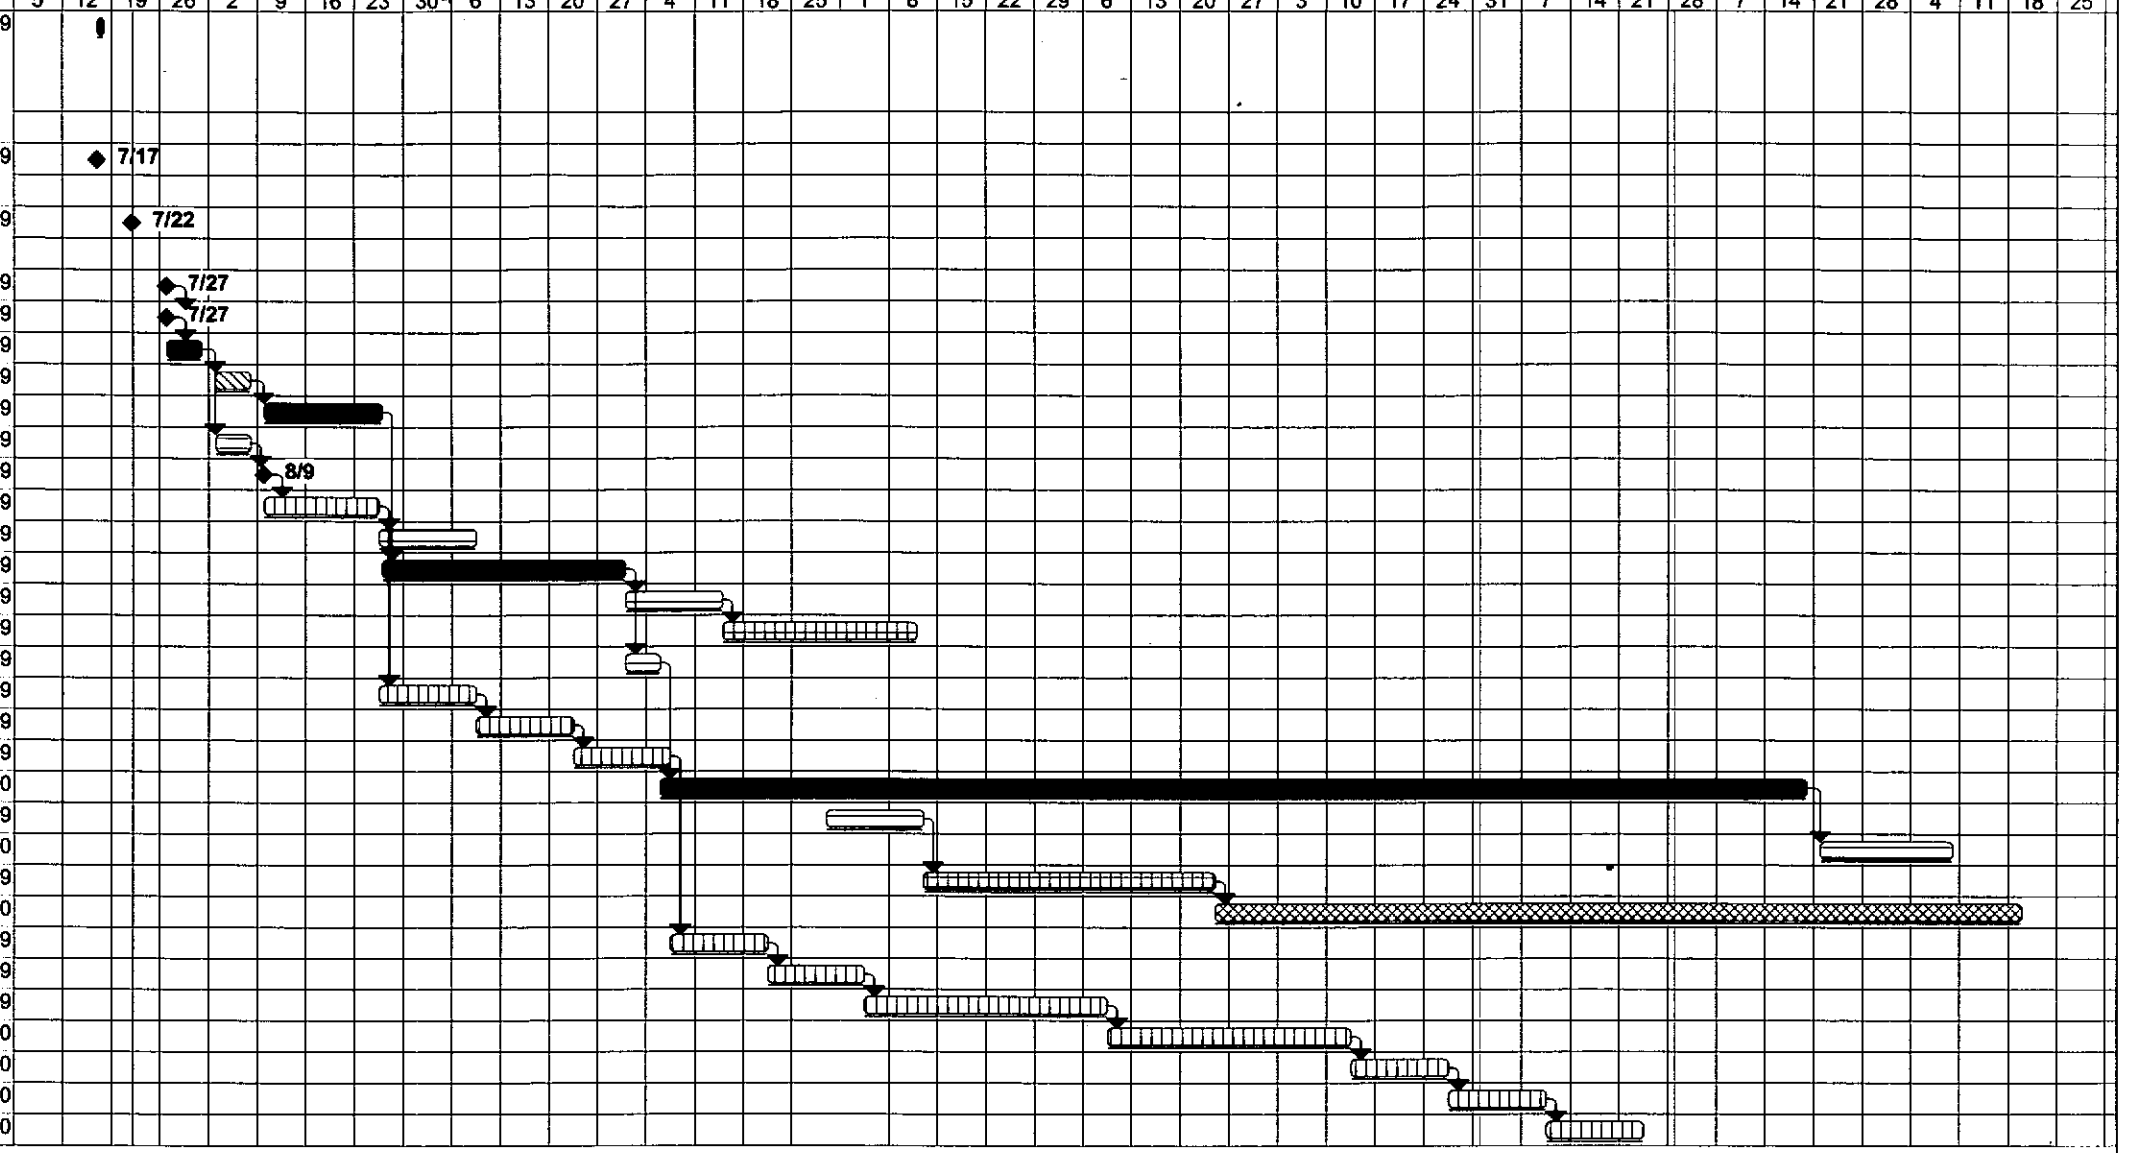

Project: Schedule.mpp
Date: Wed 7/22/09

Task | Progress | Summary | External Tasks | Deadline
Split | Milestone | Project Summary | External Milestone
